

TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	14/08/2025
Project Location:	Geraldton	Day:	Thursday
Project Number:	TCD-1816	Start:	6:00
Report Number:	80	Finish:	17:00

WEATHER & GROUND CONDITIONS

Temperature: 19 degrees    Wind: 43 km/h WSW    Precip: 10.2mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	10.5
GRIFFITHS, Daniel	Project Manager	11				Laurent Levy	Operator	10
O'SHEA, John	Senior Project Engineer					Daniel McAuffile	Operator	10
GRIFFITHS, Ashley	Supervisor	10				Jachai Griffiths	Operator	
LOW, June	HSET					O'Brian, Jamie	Operator	10.5
SKINNER,JAMIE	SUPERVISOR	11				O'Reilly,James	Operator	10
						Simpson,Joshua	Labourer	10
						Chester, Matt	Gas Fitter	
						Mounsey, Matt	Gas Fitter	
						Herring, Levin	Gas Fitter	
						Mosley,Joshua	Surveyor	2
Total Indirect Personnel onsite:	32					Total Subcontractor on-site:	7	
Total Indirect Personnel hours:	32					Total Subcontractor hours:	63	
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	5	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04		Sea Container 20ft	951200	1
Positrak	AMG 025	10				Site Sentry Tower		2
Watercart	WC04	5				Skip Bin		1
8T Excavator	AMG 014	10				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03							
Positrak SSL	SSL08	10						
Grader	SLS01							
5t Excavator	AMG 007	10						
1.5 Excavator	AMG 009	10						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:		60						

DELAYS-OPPORTUNITY

Awaiting Detail on Centrelink Carpark  
Awaiting Crossing Details for Forrest Street  
Awaiting Direction on Service Clash Forrest Street

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Return to Work
TCD - Daily Safety Focus:	Simops
Hazards Reported:	Nil
Incident Free Days	1
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA



COMMUNICATIONS

TGS MB1119-05 Scheme D implemented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

.Underground services - Gas main install and welding      .Kiosk/Transformer install and switching  
.Lot 119 Gravel 30mm layer- Stock-piling excess      .Sub-base placement on centrelink ramp  
.Importing of Basecourse material      .Widening of Ally-way  
.Balancing of Basecourse material@Bayly to Forrest street



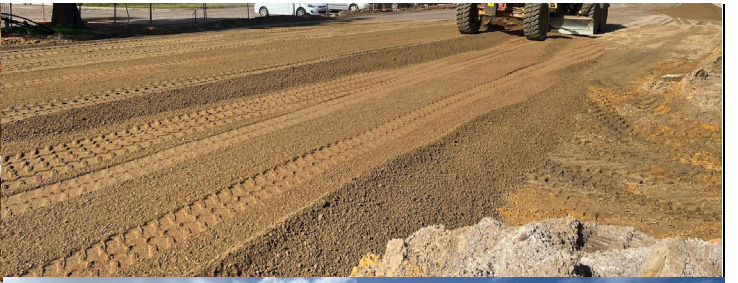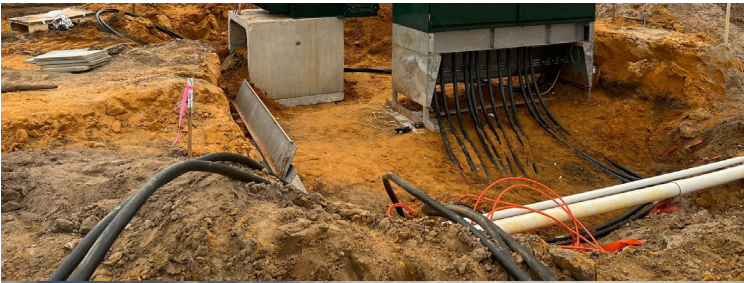

TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	15/08/2025
Project Location:	Geraldton	Day:	Friday
Project Number:	TCD-1816	Start:	6:00
Report Number:	81	Finish:	17:00

WEATHER & GROUND CONDITIONS

Temperature: 18 degrees    Wind: 35 km/h E    Precip: 0mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	10.5
GRIFFITHS, Daniel	Project Manager	9				Laurent Levy	Operator	10
O'SHEA, John	Senior Project Engineer					Daniel McAuffile	Operator	10
GRIFFITHS, Ashley	Supervisor	6				Jachai Griffiths	Operator	
LOW, June	HSET					O'Brian, Jamie	Operator	10.5
SKINNER,JAMIE	SUPERVISOR	11.5				O'Reilly,James	Operator	
						Chester, Matt	Gas Fitter	
						Mounsey, Matt	Gas Fitter	
						Herring, Levin	Gas Fitter	
						Mosley,Joshua	Surveyor	2
Total Indirect Personnel onsite:	3					Total Subcontractor on-site:		5
Total Indirect Personnel hours:	26.5					Total Subcontractor hours:		43
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	5	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04		Sea Container 20ft	951200	1
Positrak	AMG 025	10				Site Sentry Tower		2
Watercart	WC04	5				Skip Bin		1
8T Excavator	AMG 014	10				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03							
Positrak SSL	SSL08	10						
Grader	SLS01							
5t Excavator	AMG 007	10						
1.5 Excavator	AMG 009	10						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:		60						

DELAYS-OPPORTUNITY

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Return to Work
TCD - Daily Safety Focus:	Simops
Hazards Reported:	Nil
Incident Free Days	2
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-05 Scheme D impletmented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

.Balancing of Basecourse material@Bayly to Forrest street	.Concreting of Watermain bends
.Rolling Sub-base material	
.Trimming pick-ups	
.Soil test Basecourse@Bayly to Forrest st	



Photos

