



TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	27/05/2025
Project Location:	Geraldton	Day:	Tuesday
Project Number:	TCD-1816	Start:	7:00
Report Number:	17	Finish:	16:00

WEATHER & GROUND CONDITIONS

Temperature: 23 degrees Wind: 15 km/h N Precip: 0mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khagan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	10
GRIFFITHS, Ashley	Supervisor	10				Daniel McAuffie	Operator	10
LOW, June	HSET	10				Jachai Griffiths	Operator	
						O'Brian, Jamie	Operator	10
Total Indirect Personnel onsite:	3					Total Subcontractor on-site:	4	
Total Indirect Personnel hours:	30					Total Subcontractor hours:	40	
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18		Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04	1	Sea Container 20ft	951200	1
Positrak	AMG 025	5				Site Sentry Tower		2
Watercart	WC04	10				Skip Bin		1
8T Excavator	AMG 014	10				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03	10						
Grader	SLS01	10						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:		45						

DELAYS-OPPORTUNITY

Issues with existing basecourse in lots identified

HSEQ MESSAGES

TCD - Monthly Safety Focus:	JHA
TCD - Daily Safety Focus:	Plant on Plant Interaction
Hazards Reported:	Nil
Incident Free Days	21
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

Potential issue identified with existing gravel carpark tbc

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Ongoing mixing of basecourse with clean won material

Laying of Pipe into Western Culverts

TCD internal HSE audit Commenced

PHOTOS





TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	28/05/2025
Project Location:	Geraldton	Day:	Wednesday
Project Number:	TCD-1816	Start:	7:00
Report Number:	18	Finish:	16:00

WEATHER & GROUND CONDITIONS

Temperature: 27 degrees Wind: 33 km/h W Precip: 0mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khagan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	10
GRIFFITHS, Ashley	Supervisor	10				Daniel McAuffie	Operator	10
LOW, June	HSET	10				Jachai Griffiths	Operator	
						O'Brian, Jamie	Operator	10
Total Indirect Personnel onsite:	3					Total Subcontractor on-site:	4	
Total Indirect Personnel hours:	30					Total Subcontractor hours:	40	
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18		Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04	1	Sea Container 20ft	951200	1
Positrak	AMG 025	5				Site Sentry Tower		2
Watercart	WC04	10				Skip Bin		1
8T Excavator	AMG 014	10				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03	10						
Grader	SLS01	10						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:		45						

DELAYS-OPPORTUNITY

Issues with existing basecourse in lots identified

HSEQ MESSAGES

TCD - Monthly Safety Focus:	JHA
TCD - Daily Safety Focus:	Lifting
Hazards Reported:	Nil
Incident Free Days	22
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

Potential issue identified with existing gravel carpark tbc

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Ongoing mixing of basecourse with clean won material

Ongoing Excavation of Northern Culvert Lines

Progress Meeting Onsite

Asbestos Discovered in Northern Lots

TCD internal HSE audit ongoing





TCD DAILY FIELD REPORT

Project Name: Batavia Station Square **Date:** 29/05/2025
Project Location: Geraldton **Day:** Thursday
Project Number: TCD-1816 **Start:** 7:00
Report Number: 19 **Finish:** 16:00

WEATHER & GROUND CONDITIONS

Temperature: 25 degrees **Wind:** 29 km/h SW **Precip:** 2mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	10
GRIFFITHS, Ashley	Supervisor	10				Daniel McAuffie	Operator	10
LOW, June	HSET	10				Jachai Griffiths	Operator	
						O'Brian, Jamie	Operator	10
Total Indirect Personnel onsite:	3					Total Subcontractor on-site:	4	
Total Indirect Personnel hours:	30					Total Subcontractor hours:	40	
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	2	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04	1	Sea Container 20ft	951200	1
Positrak	AMG 025	5				Site Sentry Tower		2
Watercart	WC04	7				Skip Bin		1
8T Excavator	AMG 014	10				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03	10						
Grader	SLS01	10						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:		44						

DELAYS-OPPORTUNITY

Issues with existing basecourse in lots identified

HSEQ MESSAGES

TCD - Monthly Safety Focus:	JHA
TCD - Daily Safety Focus:	Asbestos
Hazards Reported:	Nil
Incident Free Days	24
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

Potential issue identified with existing gravel carpark tbc

Basecourse Identified in Lot 119

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)


Ongoing mixing of basecourse with clean won material

Ongoing Placement of Liners and Pipework in Trench

Asbestos Removed in Northern Lots

TCD internal HSE audit Complete

PHOTOS

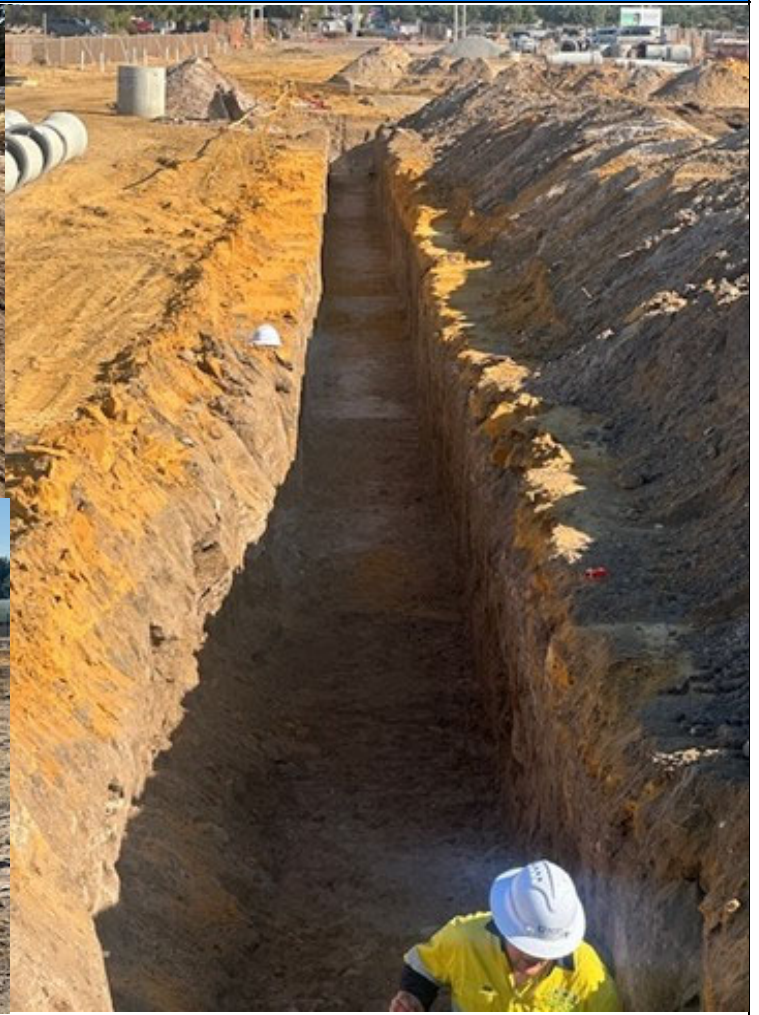



TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	30/05/2025
Project Location:	Geraldton	Day:	Friday
Project Number:	TCD-1816	Start:	7:00
Report Number:	20	Finish:	16:00

WEATHER & GROUND CONDITIONS

Temperature: 24 degrees Wind: 21 km/h S Precip: 16mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	8
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	8
GRIFFITHS, Ashley	Supervisor					Daniel McAuffie	Operator	8
LOW, June	HSET					Jachai Griffiths	Operator	
						O'Brian, Jamie	Operator	8
Total Indirect Personnel onsite:	1					Total Subcontractor on-site:		4
Total Indirect Personnel hours:	10					Total Subcontractor hours:		32
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	2	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04	1	Sea Container 20ft	951200	1
Positrak	AMG 025					Site Sentry Tower		2
Watercart	WC04					Skip Bin		1
8T Excavator	AMG 014	5				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03	5						
Grader	SLS01	5						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:		17						

DELAYS-OPPORTUNITY

Issues with existing basecourse in lots identified

HSEQ MESSAGES

TCD - Monthly Safety Focus:	JHA
TCD - Daily Safety Focus:	Asbestos
Hazards Reported:	Nil
Incident Free Days	25
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

Potential issue identified with existing gravel carpark tbc

Rain Affected Day Minimal Production

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Mudding of Pits
Grader Works Stopped to prevent worsening of site conditions



TCD DAILY FIELD REPORT		
Project Name:	Batavia Station Square	Date: 31/05/2025
Project Location:	Geraldton	Day: Saturday
Project Number:	TCD-1816	Start: 7:00
Report Number:	21	Finish: 16:00

WEATHER & GROUND CONDITIONS		
Temperature: 24 degrees	Wind: 15 km/h S	Precip: 0.2mm

PERSONNEL								
TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	
GRIFFITHS, Ashley	Supervisor					Daniel McAuffie	Operator	6
LOW, June	HSET					Jachai Griffiths	Operator	
						O'Brian, Jamie	Operator	
Total Indirect Personnel onsite:	1					Total Subcontractor on-site:	1	
Total Indirect Personnel hours:	10					Total Subcontractor hours:	6	
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT								
Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	2	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04	1	Sea Container 20ft	951200	1
Positrak	AMG 025					Site Sentry Tower		2
Watercart	WC04	2				Skip Bin		1
8T Excavator	AMG 014					Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03							
Grader	SLS01	2						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:		6						

DELAYS-OPPORTUNITY		
Issues with existing basecourse in lots identified		

HSEQ MESSAGES		
TCD - Monthly Safety Focus:	JHA	
TCD - Daily Safety Focus:	Asbestos	
Hazards Reported:	Nil	
Incident Free Days	23	
Other Notes		

INCIDENTS & REPORTS		
	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS		
Potential issue identified with existing gravel carpark tbc		

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)		
Boxout of Road		
Grader Works Stopped to prevent worsening of site conditions		
Review Barricading for Long Weekend		

PHOTOS

