



TCD DAILY FIELD REPORT

Project Name: Batavia Station Square
Project Location: Geraldton
Project Number: TCD-1816
Report Number: 50

Date: 10/07/2025
Day: Thursday
Start: 7:00
Finish: 17:00

WEATHER & GROUND CONDITIONS

Temperature: 19 degrees **Wind:** 35 km/h E **Precip:** 0 mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	8
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	10
O'SHEA, John	Senior Project Engineer					Daniel McAuffie	Operator	8
GRIFFITHS, Ashley	Supervisor	10				Jachai Griffiths	Operator	10
LOW, June	HSET					O'Brian, Jamie	Operator	10
						Rixon, Ian	Operator	8
						Goodwin, Noah	Labourer	8
						Chester, Matt	Gas Fitter	
						Mounsey, Matt	Gas Fitter	
						Herring, Levin	Gas Fitter	
Total Indirect Personnel onsite:	2					Total Subcontractor on-site:		7
Total Indirect Personnel hours:	20					Total Subcontractor hours:		62
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	10	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15	10	6 Wheel Tipper	AMG04		Sea Container 20ft	951200	1
Positrak	AMG 025	10				Site Sentry Tower		2
Watercart	WC04	5				Skip Bin		1
8T Excavator	AMG 014	10				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03							
Positrak SSL	SSL08	5						
Grader	SLS01							
1.5 Excavator	AMG 009	10						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:		60						

DELAYS-OPPORTUNITY

Watercorp unable to provide pressure main shut down 5/7/25

HSEQ MESSAGES

TCD - Monthly Safety Focus: Return to Work
TCD - Daily Safety Focus: Plant on Plant
Hazards Reported: Nil
Incident Free Days 52
Other Notes

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA


COMMUNICATIONS

TGS MB1119-05 Scheme D impletmented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Installed temp fencing to foreshire drive footpath
Ongoing underground services
Commenced Drainage to 525 Line

PHOTOS

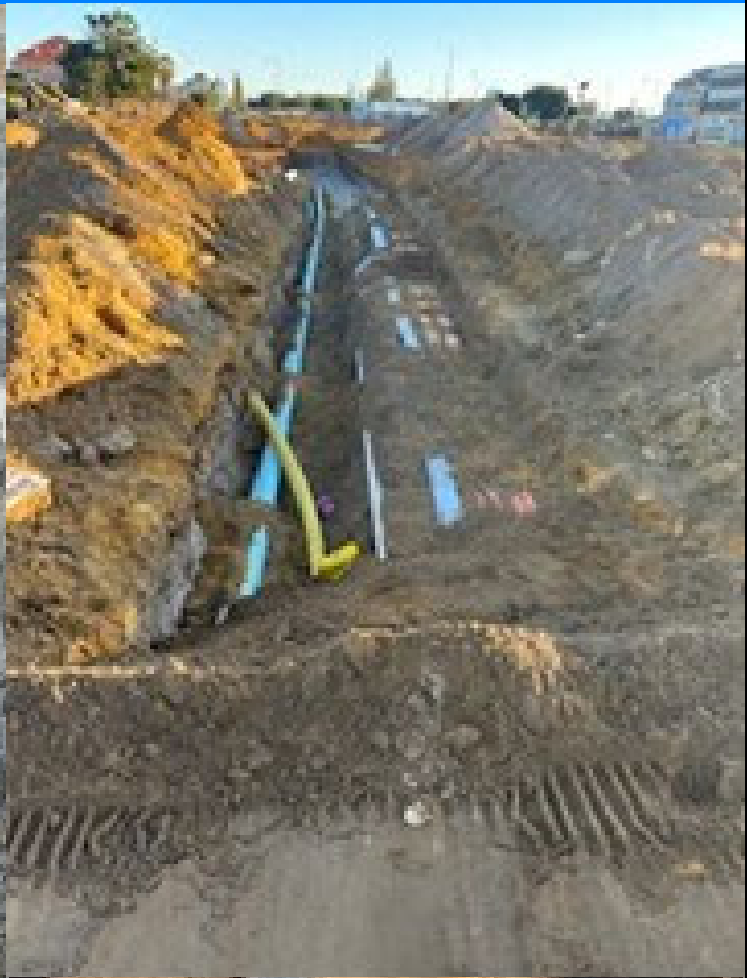



TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	11/07/2025
Project Location:	Geraldton	Day:	Friday
Project Number:	TCD-1816	Start:	7:00
Report Number:	51	Finish:	17:00

WEATHER & GROUND CONDITIONS

Temperature: 20 degrees Wind: 33 km/h NNE Precip: 0 mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	8
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	10
O'SHEA, John	Senior Project Engineer					Daniel McAuffile	Operator	8
GRIFFITHS, Ashley	Supervisor	10				Jachai Griffiths	Operator	10
LOW, June	HSET					O'Brian, Jamie	Operator	10
						Rixon, Ian	Operator	8
						Goodwin, Noah	Labourer	8
						Chester, Matt	Gas Fitter	5
						Mounsey, Matt	Gas Fitter	5
						Herring, Levin	Gas Fitter	5
Total Indirect Personnel onsite:	2					Total Subcontractor on-site:	10	
Total Indirect Personnel hours:	20					Total Subcontractor hours:	77	
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	5	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04		Sea Container 20ft	951200	1
Positrak	AMG 025	10				Site Sentry Tower		2
Watercart	WC04	5				Skip Bin		1
8T Excavator	AMG 014	10				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03							
Positrak SSL	SSL08	5						
Grader	SLS01							
5t Excavator	AMG 007	7						
1.5 Excavator	AMG 009	5						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:		47						

DELAYS-OPPORTUNITY

New irrigation design received

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Return to Work
TCD - Daily Safety Focus:	Working in Trenches
Hazards Reported:	Nil
Incident Free Days	53
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-05 Scheme D impletmented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Ongoing underground services

Ongoing Drainage to 525 Line

Preparation to watercorp shut down





TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	12/07/2025
Project Location:	Geraldton	Day:	Saturday
Project Number:	TCD-1816	Start:	7:00
Report Number:	52	Finish:	17:00

WEATHER & GROUND CONDITIONS

Temperature: 20 degrees Wind: 28 km/h SW Precip: 2 mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	8
GRIFFITHS, Daniel	Project Manager					Laurent Levy	Operator	10
O'SHEA, John	Senior Project Engineer					Daniel McAuffile	Operator	8
GRIFFITHS, Ashley	Supervisor	10				Jachai Griffiths	Operator	10
LOW, June	HSET					O'Brian, Jamie	Operator	
						Rixon, Ian	Operator	8
						Goodwin, Noah	Labourer	8
						Chester, Matt	Gas Fitter	
						Mounsey, Matt	Gas Fitter	
						Herring, Levin	Gas Fitter	
Total Indirect Personnel onsite:	1					Total Subcontractor on-site:		6
Total Indirect Personnel hours:	10					Total Subcontractor hours:		52
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	5	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04		Sea Container 20ft	951200	1
Positrak	AMG 025	10				Site Sentry Tower		2
Watercart	WC04	5				Skip Bin		1
8T Excavator	AMG 014	10				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03							
Positrak SSL	SSL08	5						
Grader	SLS01							
5t Excavator	AMG 007	7						
1.5 Excavator	AMG 009	5						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:		47						

DELAYS-OPPORTUNITY

APRA Shutdown

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Return to Work
TCD - Daily Safety Focus:	APRA Works
Hazards Reported:	Nil
Incident Free Days	54
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-05 Scheme D impletmented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Ongoing underground services
Passed 525 and 600 Pipe Beneath sewer pressure main

PHOTOS

