



TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square
Project Location:	Geraldton
Project Number:	TCD-1816
Report Number:	27

Date: 10/06/2025
Day: Tuesday
Start: 7:00
Finish: 17:00

WEATHER & GROUND CONDITIONS

Temperature: 24 degrees Wind: 44 km/h WSW Precip: 0mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	10
O'SHEA, John	Senior Project Engineer					Daniel McAuffle	Operator	10
GRIFFITHS, Ashley	Supervisor					Jachai Griffiths	Operator	
LOW, June	HSET					O'Brian, Jamie	Operator	10
Total Indirect Personnel onsite:	1					Total Subcontractor on-site:		4
Total Indirect Personnel hours:	10					Total Subcontractor hours:		40
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant & Equipment									
Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty	
Komatsu WA320	FWL18	5	Hilux	DLV90	1	Office 40ft	9255540	1	
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04	1	Sea Container 20ft	951200	1	
Positrak	AMG 025					Site Sentry Tower		2	
Watercart	WC04	10				Skip Bin		1	
8T Excavator	AMG 014					Hydrocarbon Bund		1	
6 Wheel Tipper	AMG 008					Temp Fence		1	
Padfoot/ Smooth Drum Roller	RR 03	5							
Grader	SLS01	10							
0	Repairs Required	N/A							
0	Scheduled Service	N/A							
0	Repairs required but operable	N/A							

Total Plant and Equipment Hours:

DELAYS-OPPORTUNITY

HSEQ MESSAGES		
TCD - Monthly Safety Focus:	Safe Driving	
TCD - Daily Safety Focus:	Truck Movements Internal	
Hazards Reported:	Nil	
Incident Free Days	29	
Other Notes		

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Safe Driving
TCD - Daily Safety Focus:	Truck Movements Internal
Hazards Reported:	Nil
Incident Free Days	29
Others Noted:	

Other Notes

INCIDENTS & REPORTS

INCIDENTS & REPORTS		
	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS


TGS MB1119-01 Implemented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Placement of fill to Northern Lots

Placement of fill to Northern Line

PHOTOS

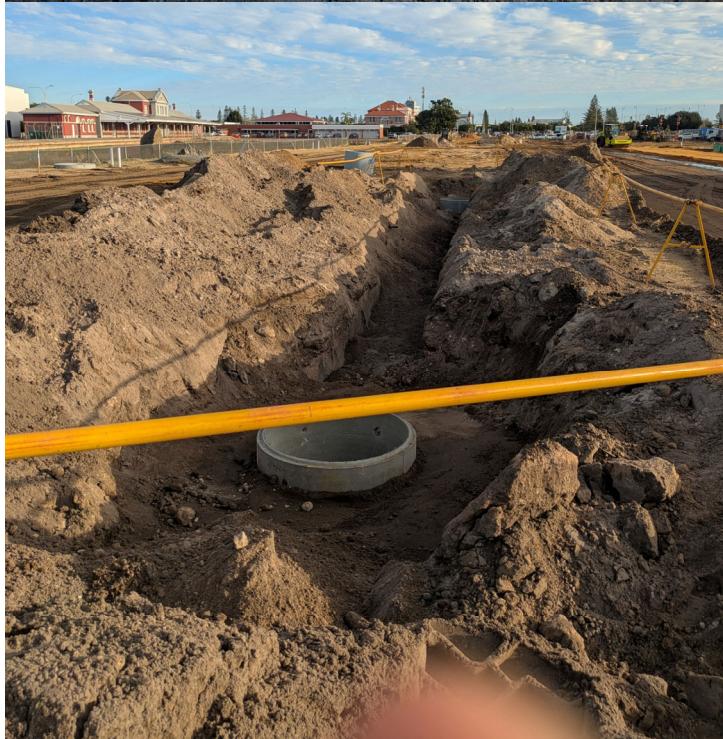



TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square
Project Location:	Geraldton
Project Number:	TCD-1816
Report Number:	28

Date:	11/06/2025
Day:	Wednesday
Start:	7:00
Finish:	17:00

WEATHER & GROUND CONDITIONS

Temperature: 21 degrees **Wind:** 28 km/h E **Precip:** 0.4mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	10
O'SHEA, John	Senior Project Engineer	10				Daniel McAuffle	Operator	10
GRIFFITHS, Ashley	Supervisor	10				Jachai Griffiths	Operator	10
LOW, June	HSET					O'Brian, Jamie	Operator	10
Total Indirect Personnel onsite:	3					Total Subcontractor on-site:	5	
Total Indirect Personnel hours:	30					Total Subcontractor hours:	50	
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant & Equipment									
Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty	
Komatsu WA320	FWL18	5	Hilux	DLV90	1	Office 40ft	9255540	1	
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04	1	Sea Container 20ft	951200	1	
Positrak	AMG 025					Site Sentry Tower		2	
Watercart	WC04	10				Skip Bin		1	
8T Excavator	AMG 014					Hydrocarbon Bund		1	
6 Wheel Tipper	AMG 008					Temp Fence		1	
Padfoot/ Smooth Drum Roller	RR 03	5							
Grader	SLS01	10							
0	Repairs Required	N/A							
0	Scheduled Service	N/A							
0	Repairs required but operable	N/A							

Total Plant and Equipment Hours:

DELAYS-OPPORTUNITY

HSEQ MESSAGES		
TCD - Monthly Safety Focus:	Safe Driving	
TCD - Daily Safety Focus:	I truck Movements Internal	
Hazards Reported:	Nil	
Incident Free Days	29	
Other Notes		

HSEQ MESSAGES

TODAY'S MESSAGE	
TCD - Monthly Safety Focus:	Safe Driving
TCD - Daily Safety Focus:	Truck Movements Internal
Hazards Reported:	Nil
Incident Free Days	29
Others Noted:	

Other Notes

INCIDENTS & REPORTS

INCIDENTS & REPORTS		
	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-01 Implemented

Progress Meeting

PRODUCTION (CON)

Placement of fill to Northern

Drainage Patch

Drainage Patching

TCD DAILY FIELD REPORT

Project Name: Batavia Station Square
 Project Location: Geraldton
 Project Number: TCD-1816
 Report Number: 29

Date: 12/06/2025
 Day: Thursday
 Start: 7:00
 Finish: 17:00

WEATHER & GROUND CONDITIONS

Temperature: 21 degrees Wind: 33 km/h NE Precip: 0mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	10
O'SHEA, John	Senior Project Engineer	10				Daniel McAuffile	Operator	10
GRIFFITHS, Ashley	Supervisor	10				Jachai Griffiths	Operator	10
LOW, June	HSET	10				O'Brian, Jamie	Operator	10
Total Indirect Personnel onsite:	4					Total Subcontractor on-site:		5
Total Indirect Personnel hours:	40					Total Subcontractor hours:		50
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	5	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04	1	Sea Container 20ft	951200	1
Positrak	AMG 025	5				Site Sentry Tower		2
Watercart	WC04	10				Skip Bin		1
8T Excavator	AMG 014	5				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03	10						
Grader	SLS01	10						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:	45							

DELAYS-OPPORTUNITY

HSEQ MESSAGES		
TCD - Monthly Safety Focus: Safe Driving		
TCD - Daily Safety Focus: Truck Movements Internal		
Hazards Reported: Nil		
Incident Free Days: 30		
Other Notes:		

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-01 Implemented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Placement of fill to Northern Lots
Carpark Repairs

PHOTOS



TCD DAILY FIELD REPORT

Project Name: Batavia Station Square Date: 14/06/2025
 Project Location: Geraldton Day: Saturday
 Project Number: TCD-1816 Start: 7:00
 Report Number: 31 Finish: 15:00

WEATHER & GROUND CONDITIONS

Temperature: 23 degrees Wind: 24 km/h W Precip: 0mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	
GRIFFITHS, Daniel	Project Manager					Laurent Levy	Operator	8
O'SHEA, John	Senior Project Engineer					Daniel McAuffile	Operator	
GRIFFITHS, Ashley	Supervisor	9				Jachai Griffiths	Operator	8
LOW, June	HSET					O'Brian, Jamie	Operator	
Total Indirect Personnel onsite:	1					Total Subcontractor on-site:	2	
Total Indirect Personnel hours:	9					Total Subcontractor hours:	16	
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	8	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04	1	Sea Container 20ft	951200	1
Positrak	AMG 025					Site Sentry Tower		2
Watercart	WC04					Skip Bin		1
8T Excavator	AMG 014	5				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03							
Grader	SLS01							
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:		13						

DELAYS-OPORTUNITY

Removed Fence to Northern Lots
 Installed Temp Fence
 Test Pitted Area for Gravel

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Safe Driving
TCD - Daily Safety Focus:	Manual Handling
Hazards Reported:	Nil
Incident Free Days	32
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS
PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Placement of fill to Northern Lots
 Carpark Repairs Patch Holes near Station Platform

PHOTOS





TCD DAILY FIELD REPORT

Project Name: Batavia Station Square Date: 16/06/2025
 Project Location: Geraldton Day: Monday
 Project Number: TCD-1816 Start: 7:00
 Report Number: 33 Finish: 17:00

WEATHER & GROUND CONDITIONS

Temperature: 24 degrees Wind: 30 km/h NE Precip: 0mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager					Laurent Levy	Operator	10
O'SHEA, John	Senior Project Engineer					Daniel McAuffile	Operator	10
GRIFFITHS, Ashley	Supervisor	10				Jachai Griffiths	Operator	10
LOW, June	HSET					O'Brian, Jamie	Operator	10
Total Indirect Personnel onsite:	1					Total Subcontractor on-site:		5
Total Indirect Personnel hours:	10					Total Subcontractor hours:		50
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	10	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04	1	Sea Container 20ft	951200	1
Positrak	AMG 025	10				Site Sentry Tower		2
Watercart	WC04	10				Skip Bin		1
8T Excavator	AMG 014					Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03	10						
Grader	SLS01	10						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:		50						

DELAYS-OPPORTUNITY

HSEQ MESSAGES		

TCD - Monthly Safety Focus: Safe Driving
 TCD - Daily Safety Focus: SIMOPS
 Hazards Reported: Nil
 Incident Free Days: 33
 Other Notes:

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-01 Implemented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Placement of fill to Northern Lots
 Commence Excavation of Gravel to Northern Lots Strip
 Removal of Dust Fence

PHOTOS





TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	17/06/2025
Project Location:	Geraldton	Day:	Tuesday
Project Number:	TCD-1816	Start:	7:00
Report Number:	33	Finish:	17:00

WEATHER & GROUND CONDITIONS

Temperature: 24 degrees Wind: 48 km/h N Precip: 0mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	10
O'SHEA, John	Senior Project Engineer					Daniel McAuffile	Operator	10
GRIFFITHS, Ashley	Supervisor	10				Jachai Griffiths	Operator	10
LOW, June	HSET					O'Brian, Jamie	Operator	10
						Rixon, Ian	Operator	10
Total Indirect Personnel onsite:	2					Total Subcontractor on-site:		6
Total Indirect Personnel hours:	20					Total Subcontractor hours:		60
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	5	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04	1	Sea Container 20ft	951200	1
Positrak	AMG 025	10				Site Sentry Tower		2
Watercart	WC04	10				Skip Bin		1
8T Excavator	AMG 014	10				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03	10						
Grader	SLS01	10						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:	55							

DELAYS-OPPORTUNITY

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Safe Driving
TCD - Daily Safety Focus:	Plant on Plant
Hazards Reported:	Nil
Incident Free Days	34
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-01 Implemented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Placement of fill to Northern Lots

Breaking up of gravel along Fenceline

PHOTOS





TCD DAILY FIELD REPORT

Project Name: Batavia Station Square
 Project Location: Geraldton
 Project Number: TCD-1816
 Report Number: 34

Date: 18/06/2025
 Day: Wednesday
 Start: 7:00
 Finish: 17:00

WEATHER & GROUND CONDITIONS

Temperature: 23 degrees Wind: 61 km/h N Precip: 31.6mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	10
O'SHEA, John	Senior Project Engineer					Daniel McAuffile	Operator	10
GRIFFITHS, Ashley	Supervisor	10				Jachai Griffiths	Operator	10
LOW, June	HSET					O'Brian, Jamie	Operator	10
						Rixon, Ian	Operator	10
Total Indirect Personnel onsite:	2					Total Subcontractor on-site:		6
Total Indirect Personnel hours:	20					Total Subcontractor hours:		60
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	5	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04	1	Sea Container 20ft	951200	1
Positrak	AMG 025					Site Sentry Tower		2
Watercart	WC04	10				Skip Bin		1
8T Excavator	AMG 014	10				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03	10						
Grader	SLS01	10						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:		45						

DELAYS-OPPORTUNITY

HSEQ MESSAGES		
TCD - Monthly Safety Focus:	Safe Driving	
TCD - Daily Safety Focus:	Public Interaction	
Hazards Reported:	Nil	
Incident Free Days	35	
Other Notes		

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-01 Implemented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Placement of fill to Northern Lots
 Foundation Prep Along Fence
 Sump Works
 Locate Joints of SPM

PHOTOS





TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	19/06/2025
Project Location:	Geraldton	Day:	Thursday
Project Number:	TCD-1816	Start:	7:00
Report Number:	35	Finish:	17:00

WEATHER & GROUND CONDITIONS

Temperature: 23 degrees Wind: 30 km/h N Precip: 0.6mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	10
O'SHEA, John	Senior Project Engineer					Daniel McAuffile	Operator	10
GRIFFITHS, Ashley	Supervisor					Jachai Griffiths	Operator	10
LOW, June	HSET					O'Brian, Jamie	Operator	10
						Rixon, Ian	Operator	10
Total Indirect Personnel onsite:	1					Total Subcontractor on-site:		6
Total Indirect Personnel hours:	10					Total Subcontractor hours:		60
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	5	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04	1	Sea Container 20ft	951200	1
Positrak	AMG 025					Site Sentry Tower		2
Watercart	WC04	10				Skip Bin		1
8T Excavator	AMG 014	10				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03	10						
Grader	SLS01	10						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:		45						

DELAYS-OPPORTUNITY

HSEQ MESSAGES		
TCD - Monthly Safety Focus:	Safe Driving	
TCD - Daily Safety Focus:	Plant on Plant Interaction	
Hazards Reported:	Nil	
Incident Free Days	36	
Other Notes		

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-01 Implemented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Placement of fill to Northern Lots

Power Startup Meeting

Location of Additional Services

Patching Drainage lines

PHOTOS





TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	20/06/2025
Project Location:	Geraldton	Day:	Friday
Project Number:	TCD-1816	Start:	7:00
Report Number:	36	Finish:	17:00

WEATHER & GROUND CONDITIONS

Temperature: 23 degrees Wind: 67 km/h N Precip: 8mm (Geraldton Airport)

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	6
GRIFFITHS, Daniel	Project Manager	8				Laurent Levy	Operator	6
O'SHEA, John	Senior Project Engineer					Daniel McAuffile	Operator	6
GRIFFITHS, Ashley	Supervisor					Jachai Griffiths	Operator	
LOW, June	HSET					O'Brian, Jamie	Operator	6
						Rixon, Ian	Operator	6
Total Indirect Personnel onsite:	1					Total Subcontractor on-site:		5
Total Indirect Personnel hours:	8					Total Subcontractor hours:		30
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	3	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04	1	Sea Container 20ft	951200	1
Positrak	AMG 025					Site Sentry Tower		2
Watercart	WC04					Skip Bin		1
8T Excavator	AMG 014					Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03	6						
Grader	SLS01	6						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:		15						

DELAYS-OPPORTUNITY

HSEQ MESSAGES		
TCD - Monthly Safety Focus:	Safe Driving	
TCD - Daily Safety Focus:	Truck Routes Onsite	
Hazards Reported:	Nil	
Incident Free Days	37	
Other Notes		

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-01 Implemented

Works Stopped Early Due to Heavy Rain

APRA Signed

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Placement of fill to Northern Lots

Watercorp Pipelaying Course

Rocking Drainge Sump

PHOTOS





TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	23/06/2025
Project Location:	Geraldton	Day:	Monday
Project Number:	TCD-1816	Start:	7:00
Report Number:	37	Finish:	17:00

WEATHER & GROUND CONDITIONS

Temperature: 19 degrees Wind: 41 km/h SE Precip: 3.4mm (31mm encountered over the weekend)

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	
O'SHEA, John	Senior Project Engineer					Daniel McAuffile	Operator	10
GRIFFITHS, Ashley	Supervisor					Jachai Griffiths	Operator	
LOW, June	HSET					O'Brian, Jamie	Operator	10
						Rixon, Ian	Operator	10
Total Indirect Personnel onsite:	1					Total Subcontractor on-site:		4
Total Indirect Personnel hours:	10					Total Subcontractor hours:		40
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	10	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15	10	6 Wheel Tipper	AMG04	1	Sea Container 20ft	951200	1
Positrak	AMG 025					Site Sentry Tower		2
Watercart	WC04					Skip Bin		1
8T Excavator	AMG 014					Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03	10						
Grader	SLS01	10						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:		40						

DELAYS-OPPORTUNITY

HSEQ MESSAGES		
TCD - Monthly Safety Focus:	Safe Driving	
TCD - Daily Safety Focus:	Managing Weather	
Hazards Reported:	Nil	
Incident Free Days	38	
Other Notes		

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-01 Implemented

No works over the weekend due to weather

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Import Fill to Lot 199 and Verges

Mitigating Water to allow trucks to safely pass through site

PHOTOS

