



TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	10/09/2025
Project Location:	Geraldton	Day:	Wednesday
Project Number:	TCD-1816	Start:	6:00
Report Number:	103	Finish:	18:00

WEATHER & GROUND CONDITIONS

Temperature: 21 degrees Wind: 43km/h E Precip: 0 mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager		Asmatullayev, Ikhtiyar	Labourer		Khegan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager	12	Hanly, Thomas	Operator		Daniel McAuffle	Operator	10
O'SHEA, John	Senior Project Engineer		McGahon,Aideen	Opetaor	12	Jachai Griffiths	Operator	
GRIFFITHS, Ashley	Supervisor					O'Brian, Jamie	Operator	10
LOW, June	HSET					O'Reilly,James	Operator	
SKINNER, Jamie	Supervisor	12				Dixon, Warren	Irrigation Installer	
TONER, Ultan	Supervisor	12				Mosley,Joshua	Surveyor	5
Total Indirect Personnel onsite:	3							
Total Indirect Personnel hours:	36							
Total Direct Personnel onsite:	3							
Total Direct Personnel hours:	12							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	5	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		Hilux	DLV04	1	Sea Container 20ft	951200	1
Watercart	WC04					Site Sentry Tower		2
8T Excavator	AMG 014					Skip Bin		1
Mini Tipper	SLS05					Hydrocarbon Bund		1
1t Excavator	SLS03	5				Temp Fence		1
14t Excavator with GPS	EX153	5						
5t Excavator	A118	5						
Padfoot/ Smooth Drum Roller	RR 03							
Multi Roller	256							
Positrak SSL	SSL08	5						
Grader	SLS01							
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0			N/A					
Total Plant and Equipment Hours:		25						

DELAYS-OPPORTUNITY

New Detail Provided on Centrelink Carpark
 Kerbing Plan reissued by TCD
 Awaiting Direction on Service Clash Forrest Street
 Awaiting Confirmation on Batters Treatment
 Awaiting finalised fencing details
 Awaiting COGG confirmation for "Ballast Pile"
 Instructions Provided for Laneway Sewer, Drainage and Light Pole Removal
 Demo and new kerb design not aligning awaiting Survey report
 Sump Levels option provided
 Confirmation of CCTV Alignment Through Crossing Provided

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Underground Services
TCD - Daily Safety Focus:	Manual Handling
Hazards Reported:	Nil
Incident Free Days	18

Other Notes

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS


TGS MB1119-05 Scheme D implemented

TGS MB1119-07B implemented (Closure Notification Upcoming)

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Service Exposure	Setting of Lids/ Concreting
Surveyor mark-up of Front of kerb	
Setting of Storm-water lids/Concreting	

Photos

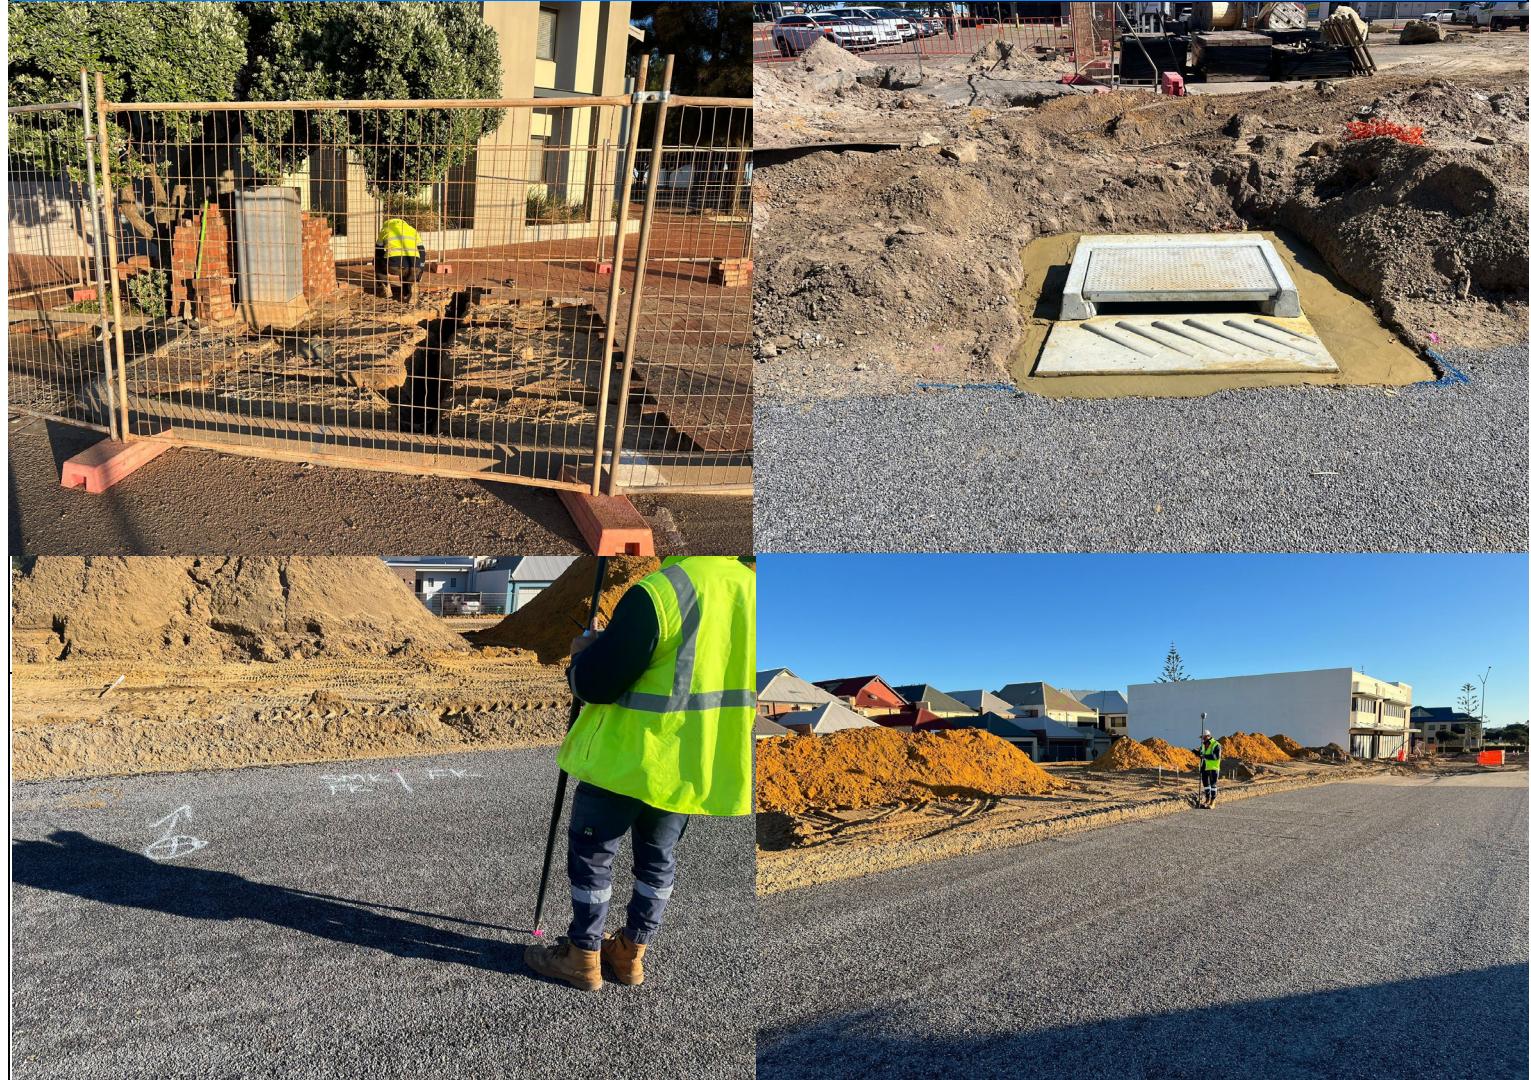

TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	11/09/2025
Project Location:	Geraldton	Day:	Thursday
Project Number:	TCD-1816	Start:	6:00
Report Number:	104	Finish:	18:00

WEATHER & GROUND CONDITIONS

Temperature: 23 degrees Wind: 39km/h ENE Precip: 0 mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager		Asmatullayev, Ikhtiyar	Labourer		Khegan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager	12	Hanly, Thomas	Operator		Daniel McAuffle	Operator	10
O'SHEA, John	Senior Project Engineer		McGahon,Aideen	Operator	12	O'Brian, Jamie	Operator	10
GRIFFITHS, Ashley	Supervisor					Mosley,Joshua	Surveyor	
THOMPSON,Cheryl	HSET							
SKINNER,Jamie	Supervisor	12				Midwest Kerbing		
Ultan,Toner	Supervisor	12				Daly,Troy	Specialist	10
						Kerbers x 3	Operator/Labourer	30
						Vac Truck Crew	Operator/Labourer	10
Total Indirect Personnel onsite:	3							
Total Indirect Personnel hours:	36							
Total Direct Personnel onsite:	1							
Total Direct Personnel hours:	12							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	5	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		Hilux	1DLV04	1	Sea Container 20ft	951200	1
Watercart	WC04					Site Sentry Tower		2
8T Excavator	AMG 014					Skip Bin		1
Mini Tipper	SLS05					Hydrocarbon Bund		1
1 t Excavator	SLS03					Temp Fence		1
14t Excavator with GPS	EX153	5						
5t Excavator	A118							
Padfoot/ Smooth Drum Roller	RR 03							
Multi Roller	256							
Positrak SSL	SSL08	5						
Grader	SLS01							
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0			N/A					
Total Plant and Equipment Hours:		15						

DELAYS-OPORTUNITY

New Detail Provided on Centrelink Carpark Demo and new kerb design not aligning awaiting Porters response
 Kerbing Plan reissued by TCD
 Awaiting Direction on Service Clash Forrest Street
 Awaiting Confirmation on Batters Treatment
 Awaiting finalised fencing details
 Awaiting COGG confirmation on "Ballast Pile"
 Instructions Provided for Laneway Sewer, Drainage and Light Pole Removal

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Underground Services
TCD - Daily Safety Focus:	Area awareness
Hazards Reported:	Nil
Incident Free Days	19
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-05 Scheme D implemented

TGS MB1119-07B implemented (Closure Notification Upcoming)

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Paving removal @ foreshore contd. Kerbers on site to start laying kerbing

Exposure of services to Foreshire Drive West for shut

Waste Removal

Photos





TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square
Project Location:	Geraldton
Project Number:	TCD-1816
Report Number:	105

Date:	12/09/2025
Day:	Friday
Start:	6:00
Finish:	18:00

WEATHER & GROUND CONDITIONS

Temperature: 27 degrees Wind: 48km/h NE Precip: 0 mm

PERSONNEL

Total Direct Personnel hours

Plant & Equipment								
Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	5	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		Hilux	1DLV04	1	Sea Container 20ft	951200	1
Watercart	WC04					Site Sentry Tower		2
8T Excavator	AMG 014					Skip Bin		1
Mini Tipper	SLS05	4				Hydrocarbon Bund		1
1 t Excavator	SLS03	3				Temp Fence		1
14t Excavator with GPS	EX153							
5t Excavator	A118	5						
Padfoot/ Smooth Drum Roller	RR 03	5						
Multi Roller	256							
Positrak SSL	SSL08	5						
Grader	SLS01							
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0			N/A					

Total Plant and Equipment Hours:

DELAYS-OPPORTUNITY

New Detal Provided on Centrelink Carpark
Kerbing Plan reissued by TCD
Awaiting Direction on Service Clash Forrest Street
Awaiting Confirmation on Batters Treatment
Awaiting finalised fencing details
Awaiting COGG confirmation on "Ballast Pile"
Instructions Provided for Laneway Sewer, Drainage and Light Pole Removal

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Underground Services
TCD - Daily Safety Focus:	Area awareness
Hazards Reported:	Nil
Incident Free Days	20
Other Notes:	

Other Notes

INCIDENTS & REPORTS

INCIDENTS & REPORTS		QTY	Comments
	INCIDENT	0	NA
	IR	0	NA
	NCR	0	NA

COMMUNICATIONS

TGS MB1119-05 Scheme D implemented

TGS MB1119-07B implemented (Closure Notification Upcoming)

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Paving removal @ foreshore	Kerbers on site contd works on FK
Import of red gravel for shut down topup	Comms/CCTV/Irrigation Exposed for trench shut works
Bedding below qas line @ foreshore completed	

Photos



Photos



TCD DAILY FIELD REPORT

Project Name: Batavia Station Square
 Project Location: Geraldton
 Project Number: TCD-1816
 Report Number: 107

Date: 15/09/2025
 Day: Monday
 Start: 6:00
 Finish: 18:00

WEATHER & GROUND CONDITIONS

Temperature: 19 degrees Wind: 52km/h SW Precip: 3.6 mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager		Asmatullayev, Ikhtiyar	Labourer	12	Khegan Brockman	Labourer	0
GRIFFITHS, Daniel	Project Manager	12	Hanly, Thomas	Operator		Daniel McAuffie	Operator	10
O'SHEA, John	Senior Project Engineer		McGahon, Aideen	Operator	13	O'Brian, Jamie	Operator	10
GRIFFITHS, Ashley	Supervisor					Mosley, Joshua	Surveyor	12
THOMPSON, Cheryl	HSET					Mullin, Connell	Operator	12
SKINNER, Jamie	Supervisor	13						
TONER, Ultan	Supervisor	13				Midwest Kerbing		
						Daly, Troy	Specialist	5
						x3 labourers	Specialist	15
						Herrings Gas		
						Herring, Chris	Gas Fitter	5
						x2 fitters	Gas Fitter	10
						Mid Coast Civil		
						Vermeer, Paul	Labourer	10
						Patroni, Rodney	Labourer	10
						Superstruct		
						Ferstat, Blair	Labourer	10
						x3 labourers	Labourer	30
						Oaks Civil		
						Traffic Controllers x5	Traffic Controller	62.5
Total Indirect Personnel onsite:	3							
Total Indirect Personnel hours:	38							
Total Direct Personnel onsite:	2					Total Subcontractor on-site:	26	
Total Direct Personnel hours:	25					Total Subcontractor hours:	201.5	

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	2	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15	6	Hilux	1DLV04	1	Sea Container 20ft	951200	1
Watercart	WC04	5				Site Sentry Tower		2
8T Excavator	AMG 014					Skip Bin		1
Mini Tipper	SLS05	8				Hydrocarbon Bund		1
1 t Excavator	SLS03	6				Temp Fence		1
14t Excavator with GPS	EX153	8						
5t Excavator	A118	5						
Padfoot/ Smooth Drum Roller	RR 03	4						
Multi Roller	256							
Positrak SSL	SSL08	7						
6 Wheel Tipper	T091	5						
Grader	SLS01							
0	Repairs Required	N/A						
0	Scheduled Service	N/A						
0		N/A						
Total Plant and Equipment Hours:		56						

DELAYS-OPPORTUNITY

New Detail Provided on Centrelink Carpark
 Kerbing Plan reissued by TCD
 Awaiting Direction on Service Clash Forrest Street
 Awaiting Confirmation on Batters Treatment
 Awaiting finalised fencing details
 Awaiting COGG confirmation on "Ballast Pile"
 Instructions Provided for Laneway Sewer, Drainage and Light Pole Removal
 Noted Additional Material needed to be removed beneath the pavers

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Underground Services
TCD - Daily Safety Focus:	Shut Down Area, Positive Comms and Keep Clear of Machinery
Hazards Reported:	Nil
Incident Free Days	20
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-05 Scheme D implemented

TGS MB1119-07A implemented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Commenced Demolition Works in Foreshore Drive Shut Down

Trenched and Backfilled, Water, Gas, Irrigation and CCTV in Foreshore Drive Shut Down

Formed and inspected Northern and Western Ramp in Foreshore Drive Shut Down

Photos



TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	16/09/2025
Project Location:	Geraldton	Day:	Tuesday
Project Number:	TCD-1816	Start:	6:00
Report Number:	108	Finish:	18:00

WEATHER & GROUND CONDITIONS

Temperature: 20 degrees Wind: 33km/h SSW Precip: 0.4 mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager		Asmatullayev, Ikhtiyar	Labourer	12	Khegan Brockman	Labourer	0
GRIFFITHS, Daniel	Project Manager	12	Hanly, Thomas	Operator		Daniel McAufflie	Operator	10
O'SHEA, John	Senior Project Engineer	12	McGahon, Aideen	Operator	12	O'Brian, Jamie	Operator	10
GRIFFITHS, Ashley	Supervisor					Mosley, Joshua	Surveyor	11
THOMPSON, Cheryl	HSET					Mullin, Connell	Operator	12
SKINNER, Jamie	Supervisor	12						
TONER, Ultan	Supervisor	12						
						Herrings Gas		
						Herring, Chris	Gas Fitter	5
						1x Labourer	Gas Fitter	5
						Mid Coast Civil		
						Vermeer, Paul	Labourer	10
						Patroni, Rodney	Labourer	10
						Superstruct		
						Ferstat, Blair	Labourer	10
						x3 Labourers	Labourer	30
						Oaks Civil		
						Traffic Controllers x5	Traffic Controller	62.5
Total Indirect Personnel onsite:	4							
Total Indirect Personnel hours:	48							
Total Direct Personnel onsite:	2							
Total Direct Personnel hours:	24							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	2	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15	6	Hilux	1DLV04	1	Sea Container 20ft	951200	1
Watercart	WC04	5				Site Sentry Tower		2
8T Excavator	AMG 014					Skip Bin		1
Mini Tipper	SLS05	8				Hydrocarbon Bund		1
1 t Excavator	SLS03	6				Temp Fence		1
14t Excavator with GPS	EX153	8						
5t Excavator	A118	5						
Padfoot/ Smooth Drum Roller	RR 03	3						
Multi Roller	256	3						
Positrak SSL	SSL08	5						
6 Wheel Tipper	T091	5						
Grader	SLS01							
0	Repairs Required		N/A					
1	Scheduled Service		Smooth Drum Roller					
0			N/A					
Total Plant and Equipment Hours:		56						

DELAYS-OPPORTUNITY

New Detail Provided on Centrelink Carpark

Kerbing Plan reissued by TCD

Awaiting Direction on Service Clash Forrest Street

Awaiting Confirmation on Batters Treatment

Awaiting finalised fencing details

Awaiting COGO confirmation on "Ballast Pile"

Instructions Provided for Laneway Sewer, Drainage and Light Pole Removal

Noted Additional Material needed to be removed beneath the pavers

Confirmed alignment shift of south eastern tie in to flush kerb alignment

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Underground Services
TCD - Daily Safety Focus:	Shut Down Area, Positive Comms and Keep Clear of Machinery
Hazards Reported:	Nil
Incident Free Days	21
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-05 Scheme D implemented

TGS MB1119-07A implemented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Ongoing Demolition Works in Foreshore Drive Shut Down
Basecourse Top up and Roll
Commenced Trimming of basecourse
Pressure Testing Completed
Connected Irrigation Mainline
Poured Northern and Western Ramp, Formed and Poured Southern Ramp

Photos





TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square
Project Location:	Geraldton
Project Number:	TCD-1816
Report Number:	109

Date:	17/09/2025
Day:	Wednesday
Start:	6:00
Finish:	18:00

WEATHER & GROUND CONDITIONS

Temperature: 21 degrees Wind: 39km/h SSW Precip: 0 mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager	12	Asmatullayev, Ikhtiyor	Labourer	12	Khegan Brockman	Labourer	0
GRIFFITHS, Daniel	Project Manager	12	Hanly, Thomas	Operator	12	Daniel McAuffile	Operator	10
O'SHEA, John	Senior Project Engineer		McGahon,Aideen	Operator	12	O'Brian, Jamie	Operator	10
GRIFFITHS, Ashley	Supervisor					Mosley,Joshua	Surveyor	11
THOMPSON,Cheryl	HSET					Mullin, Connell	Operator	12
SKINNER,Jamie	Supervisor	12						
TONER, Ultan	Supervisor	12				Mid Coast Civil		
						Vermeer, Paul	Labourer	10
						Patroni, Rodney	Labourer	10
						Superstruct		
						Ferstat, Blair	Labourer	3
						x3 Labourers	Labourer	9
						Oaks Civil		
						Traffic Controllers x5	Traffic Controller	62.5
Total Indirect Personnel onsite:	4							
Total Indirect Personnel hours:	48					Total Subcontractor on-site:	22	
Total Direct Personnel onsite:	3					Total Subcontractor hours:	137.5	
Total Direct Personnel hours:	26							

PLANT & EQUIPMENT

Plant & Equipment									
Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty	
Komatsu WA320	FWL18	2	Hilux	DLV90	1	Office 40ft	9255540	1	
Wacker Neuson DPU	DPC15		Hilux	1DLV04	1	Sea Container 20ft	951200	1	
Watercart	WC04	5				Site Sentry Tower		2	
8T Excavator	AMG 014					Skip Bin		1	
Mini Tipper	SLS05	6				Hydrocarbon Bund		1	
1 t Excavator	SLS03	7				Temp Fence		1	
14t Excavator with GPS	EX153	8							
5t Excavator	A118	8							
Padfoot/ Smooth Drum Roller	RR 03								
Multi Roller	256	3							
Positrak SSL	SSL08	8							
6 Wheel Tipper	T091	5							
Grader	SLS01								
0	Repairs Required	N/A							
1	Scheduled Service	Smooth Drum Roller							
0		N/A							
Total Plant and Equipment Hours:		52							

Total Plant and Equipment DELAYS-OPPORTUNITY

- New Detail Provided on Centrelink Carpark
- Kerbing Plan reissued by TCD
- Awaiting Direction on Service Clash Forrest Street
- Awaiting Confirmation on Batters Treatment
- Awaiting finalised fencing details
- Awaiting COGG confirmation on "Ballast Pile"
- Instructions Provided for Laneway Sewer, Drainage and Light Pole Removal
- Noted Additional Material needed to be removed beneath the pavers
- Confirmed alignment shift of south eastern tie in to flesh kerb alignment

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Underground Services
TCD - Daily Safety Focus:	Shut Down Area, Positive Comms and Keep Clear of Machinery
Hazards Reported:	Nil
Incident Free Days	22
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-05 Scheme D implemented

TGS MB1119-07A implemented

Progress Meeting

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Ongoing Basecourse Top up and Roll

Ongoing Trimming of basecourse

Removal of top

Photos





TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square
Project Location:	Geraldton
Project Number:	TCD-1816
Report Number:	110

Date: 18/09/2025
Day: Thursday
Start: 6:00
Finish: 18:00

WEATHER & GROUND CONDITIONS

Temperature: 21 degrees Wind: 39km/h SSW Precip: 0.6 mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager		Asmatullayev, Ikhtiyor	Labourer	12	Khegan Brockman	Labourer	0
GRIFFITHS, Daniel	Project Manager	12	Hanly, Thomas	Operator		Daniel McAuffle	Operator	10
O'SHEA, John	Senior Project Engineer		McGahon,Aideen	Operator	12	O'Brian, Jamie	Operator	10
GRIFFITHS, Ashley	Supervisor					Mosley,Joshua	Surveyor	11
THOMPSON,Cheryl	HSET					Mullin, Connell	Operator	12
SKINNER,Jamie	Supervisor	12						
TONER, Ultan	Supervisor	12				Mid Coast Civil		
						Vermeer, Paul	Labourer	10
						Patroni, Rodney	Labourer	10
						Oaks Civil		
						Traffic Controllers x5	Traffic Controller	62.5
Total Indirect Personnel onsite:	3							
Total Indirect Personnel hours:	36					Total Subcontractor on-site:	20	
Total Direct Personnel onsite:	2					Total Subcontractor hours:	125.5	
Total Direct Personnel hours:	24							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	2	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15	6	Hilux	1DLV04	1	Sea Container 20ft	951200	1
Watercart	WC04	5				Site Sentry Tower		2
8T Excavator	AMG 014					Skip Bin		1
Mini Tipper	SLS05	8				Hydrocarbon Bund		1
1 t Excavator	SLS03	6				Temp Fence		1
14t Excavator with GPS	EX153	8						
5t Excavator	A118	5						
Padfoot/ Smooth Drum Roller	RR 03	3						
Multi Roller	256	3						
Positrak SSL	SSL08	5						
6 Wheel Tipper	T091	5						
Grader	SLS01							
0	Repairs Required			N/A				
1	Scheduled Service			Smooth Drum Roller				
0				N/A				

Total Plant and Equipment

- New Detail Provided on Centrelink Carpark
- Kerbing Plan reissued by TCD
- Awaiting Direction on Service Clash Forrest Street
- Awaiting Confirmation on Batters Treatment
- Awaiting finalised fencing details
- Awaiting COGG confirmation on "Ballast Pile"
- Instructions Provided for Laneway Sewer, Drainage and Light Pole Removal
- Noted Additional Material needed to be removed beneath the pavers
- Confirmed alignment shift of south eastern tie in to flush kerb alignment
- Flush Kerb Alignment near paving entrance amended to avoid clash with drainage pit

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Underground Services
TCD - Daily Safety Focus:	Shut Down Area, Positive Comms and Keep Clear of Machinery
Hazards Reported:	Nil
Incident Free Days	23
Other Notes:	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-05 Scheme D implemented

TGS MB1119-07A implemented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Ongoing Basecourse Top up and Rol

Ongoing Trimming of basecourse

Raising of Pits in Shutdown Area

Trimming of batters and verges

Photos





TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square
Project Location:	Geraldton
Project Number:	TCD-1816
Report Number:	111

Date:	19/09/2025
Day:	Friday
Start:	6:00
Finish:	18:00

WEATHER & GROUND CONDITIONS

Temperature: 22 degrees Wind: 41km/h SSW Precip: 0 mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager		Asmatullayev, Ikhtiyar	Labourer	12	Khegan Brockman	Labourer	0
GRIFFITHS, Daniel	Project Manager	12	Hanly, Thomas	Operator	12	Daniel McAuffle	Operator	10
O'SHEA, John	Senior Project Engineer		McGahon,Aideen	Operator	12	O'Brian, Jamie	Operator	10
GRIFFITHS, Ashley	Supervisor					Mosley,Joshua	Surveyor	7
THOMPSON,Cheryl	HSET					Mullin, Connell	Operator	12
SKINNER,Jamie	Supervisor	12						
TONER, Ultan	Supervisor	12				Mid Coast Civil		
						Vermeer, Paul	Labourer	10
						Patroni, Rodney	Labourer	10
						Midwest Kerbing		
						Daly,Troy	Specialist	8
						x3 labourers	Specialist	24
						Oaks Civil		
						Traffic Controllers x5	Traffic Controller	62.5
Total Indirect Personnel onsite:	3							
Total Indirect Personnel hours:	36							
Total Direct Personnel onsite:	3							
Total Direct Personnel hours:	26							
						Total Subcontractor on-site:	22	
						Total Subcontractor hours:	153.5	

PLANT & EQUIPMENT

Plant & Equipment									
Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty	
Komatsu WA320	FWL18	3	Hilux	DLV90	1	Office 40ft	9255540	1	
Wacker Neuson DPU	DPC15		Hilux	1DLV04	1	Sea Container 20ft	951200	1	
Watercart	WC04	3				Site Sentry Tower		2	
8T Excavator	AMG 014					Skip Bin		1	
Mini Tipper	SLS05	5				Hydrocarbon Bund		1	
1 t Excavator	SLS03	5				Temp Fence		1	
14t Excavator with GPS	EX153	10							
5t Excavator	A118	2							
Padfoot/ Smooth Drum Roller	RR 03	2							
Multi Roller	256	3							
Positrak SSL	SSL08	5							
6 Wheel Tipper	T091	5							
Grader	SLS01								
0	Repairs Required	N/A							
1	Scheduled Service	Smooth Drum Roller							
0		N/A							
Total Plant and Equipment Hours:		43							

Total Plant and Equipment DELAYS-OPPORTUNITY

- New Detail Provided on Centrelink Carpark
- Kerbing Plan reissued by TCD
- Awaiting Direction on Service Clash Forrest Street
- Awaiting Confirmation on Batters Treatment
- Awaiting finalised fencing details
- Awaiting COGG confirmation on "Ballast Pile"
- Instructions Provided for Laneway Sewer, Drainage and Light Pole Removal
- Noted Additional Material needed to be removed beneath the pavers
- Confirmed alignment shift of south eastern tie in to flush kerb alignment

HSEQ MESSAGES

HSEQ MESSAGES	
TCD - Monthly Safety Focus:	Underground Services
TCD - Daily Safety Focus:	Shut Down Area, Positive Comms and Keep Clear of Machinery
Hazards Reported:	Nil
Incident Free Days	24
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-05 Scheme D implemented

TGS MB1119-07A implemented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Trimming of basecourse areas around the pit and final survey checks

Tidy up of paving tie ins

| Greasing of Lids

Photos

