



TCD DAILY FIELD REPORT

Project Name: Batavia Station Square
 Project Location: Geraldton
 Project Number: TCD-1816
 Report Number: 68

Date: 31/07/2025
 Day: Thursday
 Start: 7:00
 Finish: 17:00

WEATHER & GROUND CONDITIONS

Temperature: 22 degrees Wind 38km/h NNE Precip: 0 mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	
O'SHEA, John	Senior Project Engineer	10				Daniel McAuffile	Operator	10
GRIFFITHS, Ashley	Supervisor	10				O'Brian, Jamie	Operator	10
LOW, June	HSET					Simpson Josh	Operator	10
SKINNER, Jamie	Supervisor	10				Buecz, Jayden	Driller	8
						Anderson, Peter	Driller	8
						Chester, Matt	Gas Fitter	
						Mounsey, Matt	Gas Fitter	
						Herring, Levin	Gas Fitter	6
Total Indirect Personnel onsite:	4					Total Subcontractor on-site:	7	
Total Indirect Personnel hours:	40					Total Subcontractor hours:	62	
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18		Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04		Sea Container 20ft	951200	1
Positrak	AMG 025	10				Site Sentry Tower		2
Watrcart	WC04					Skip Bin		1
8T Excavator	AMG 014	10				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03	8						
Positrak SSL	SSL08	5						
Grader	SLS01	8						
5t Excavator	AMG 007							
1.5 Excavator	AMG 009	5						
5t Excavator	AA 25	10						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:	56							

DELAYS-OPPORTUNITY

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Return to Work
TCD - Daily Safety Focus:	Cutting PE pipe
Hazards Reported:	Nil
Incident Free Days	70
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA


COMMUNICATIONS

TGS MB1119-05 Scheme D implemented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Backfill of Underground Services
 Ongoing cutting of Drainage pits
 Drillers onsite Baily Street
 Commenced Subgrade Prep

Photos

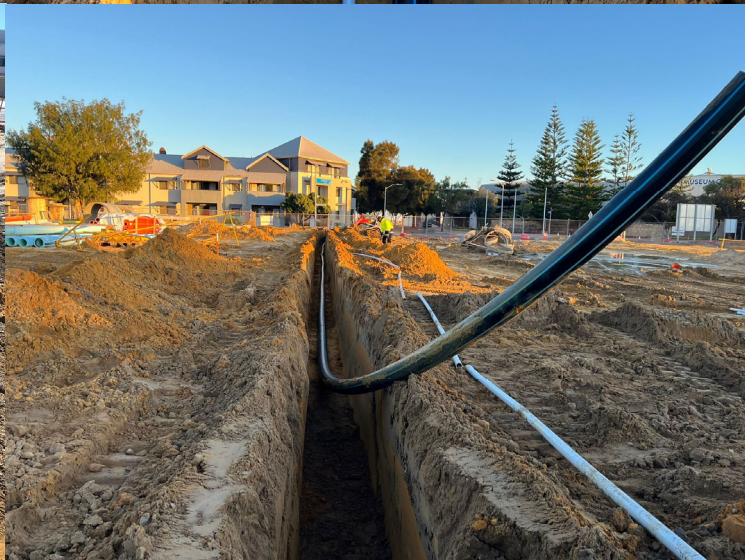



TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	1/08/2025
Project Location:	Geraldton	Day:	Friday
Project Number:	TCD-1816	Start:	7:00
Report Number:	69	Finish:	17:00

WEATHER & GROUND CONDITIONS

Temperature: 22 degrees Wind 52km/h NNE Precip: 0 mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	
O'SHEA, John	Senior Project Engineer	10				Daniel McAuffile	Operator	10
GRIFFITHS, Ashley	Supervisor					O'Brian, Jamie	Operator	10
LOW, June	HSET					Simpson, Josh	Operator	10
SKINNER, Jamie	Supervisor	10				Buecz, Jayden	Driller	8
						Anderson, Peter	Driller	8
						Chester, Matt	Gas Fitter	
						Mounsey, Matt	Gas Fitter	8
						Herring, Levin	Gas Fitter	
Total Indirect Personnel onsite:	3					Total Subcontractor on-site:	7	
Total Indirect Personnel hours:	30					Total Subcontractor hours:	64	
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18		Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15		6 Wheel Tipper	AMG04		Sea Container 20ft	951200	1
Positrak	AMG 025	10				Site Sentry Tower		2
Watercart	WC04					Skip Bin		1
8T Excavator	AMG 014	10				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03	8						
Positrak SSL	SSL08	5						
Grader	SLS01	8						
5t Excavator	AMG 007							
1.5 Excavator	AMG 009	5						
5t Excavator	AA 25	10						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:	56							

DELAYS-OPPORTUNITY

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Speaking up
TCD - Daily Safety Focus:	Plant on Plant Interaction
Hazards Reported:	Nil
Incident Free Days	71
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-05 Scheme D implemented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Ongoing cutting of Drainage pits
 Drillers onsite Baily Street
 Poly Weld Irrigation and construct thrust blocks
 Ongoing Subgrade Prep

Photos





TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	4/08/2025
Project Location:	Geraldton	Day:	Monday
Project Number:	TCD-1816	Start:	7:00
Report Number:	70	Finish:	17:00

WEATHER & GROUND CONDITIONS

Temperature: 18 degrees Wind 12 km/h WSW Precip: 0.4mm (15.8mm over the weekend)

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	
O'SHEA, John	Senior Project Engineer					Daniel McAuffile	Operator	10
GRIFFITHS, Ashley	Supervisor					O'Brian, Jamie	Operator	10
LOW, June	HSET					Simpson, Josh	Operator	10
SKINNER, Jamie	Supervisor	10				O'Reilly, James	Operator	10
						Chester, Matt	Gas Fitter	
						Mounsey, Matt	Gas Fitter	
						Herring, Levin	Gas Fitter	
Total Indirect Personnel onsite:	2					Total Subcontractor on-site:	5	
Total Indirect Personnel hours:	20					Total Subcontractor hours:	50	
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	10	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15	10	6 Wheel Tipper	AMG04		Sea Container 20ft	951200	1
Positrak	AMG 025					Site Sentry Tower		2
Watercart	WC04	2				Skip Bin		1
8T Excavator	AMG 014	6				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03	5						
Positrak SSL	SSL08	6						
Grader	SLS01	5						
5t Excavator	AMG 007							
1.5 Excavator	AMG 009							
5t Excavator	AA 25	5						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					

Total Plant and Equipment Hours:

49

DELAYS-OPPORTUNITY

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Speaking up
TCD - Daily Safety Focus:	Plant on Plant Interaction
Hazards Reported:	Nil
Incident Free Days	72
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-05 Scheme D implemented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Ongoing cutting of Drainage pits
 Drillers onsite Baily Street
 Install Flushing/ Air Valves to Mainline
 Rough Set Pits to irrigation mainline
 Install headwall in sump
 Ongoing Subgrade Prep

Photos





TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	5/08/2025
Project Location:	Geraldton	Day:	Tuesday
Project Number:	TCD-1816	Start:	7:00
Report Number:	71	Finish:	17:00

WEATHER & GROUND CONDITIONS

Temperature: 19 degrees Wind 30km/h NE Precip: 0 mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	
O'SHEA, John	Senior Project Engineer					Daniel McAuffile	Operator	10
GRIFFITHS, Ashley	Supervisor					O'Brian, Jamie	Operator	10
LOW, June	HSET					Simpson, Josh	Operator	10
SKINNER, Jamie	Supervisor	10				O'Reilly, James	Operator	10
						Chester, Matt	Gas Fitter	
						Mounsey, Matt	Gas Fitter	
						Herring, Levin	Gas Fitter	
Total Indirect Personnel onsite:	2					Total Subcontractor on-site:	5	
Total Indirect Personnel hours:	20					Total Subcontractor hours:	50	
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	5	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15	5	6 Wheel Tipper	AMG04		Sea Container 20ft	951200	1
Positrak	AMG 025					Site Sentry Tower		2
Watercart	WC04	5				Skip Bin		1
8T Excavator	AMG 014					Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03	5						
Positrak SSL	SSL08	6						
Grader	SLS01	5						
5t Excavator	AMG 007							
1.5 Excavator	AMG 009							
5t Excavator	AA 25	5						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:		36						

DELAYS-OPPORTUNITY

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Speaking up
TCD - Daily Safety Focus:	Lifting
Hazards Reported:	Nil
Incident Free Days	73
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-05 Scheme D implemented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Ongoing cutting of Drainage pits
Construction of Trial Pad
Install Flushing/ Air Valves to Mainline
Pushed Laterals through sleeve
Rough Set Pits to irrigation mainline
Install headwall in sump
Ongoing Subgrade Prep

Photos





TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	6/08/2025
Project Location:	Geraldton	Day:	Wednesday
Project Number:	TCD-1816	Start:	7:00
Report Number:	72	Finish:	17:00

WEATHER & GROUND CONDITIONS

Temperature: 19 degrees Wind No reading from BOM km/h N Precip: 0 mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	10
O'SHEA, John	Senior Project Engineer	10				Daniel McAuffile	Operator	10
GRIFFITHS, Ashley	Supervisor	10				O'Brian, Jamie	Operator	10
LOW, June	HSET					Simpson, Josh	Operator	10
SKINNER, Jamie	Supervisor	10				O'Reilly, James	Operator	10
						Chester, Matt	Gas Fitter	
						Mounsey, Matt	Gas Fitter	
						Herring, Levin	Gas Fitter	
Total Indirect Personnel onsite:	4					Total Subcontractor on-site:	6	
Total Indirect Personnel hours:	40					Total Subcontractor hours:	60	
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	5	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15	5	6 Wheel Tipper	AMG04		Sea Container 20ft	951200	1
Positrak	AMG 025					Site Sentry Tower		2
Watercart	WC04	8				Skip Bin		1
8T Excavator	AMG 014	6				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03	10						
Positrak SSL	SSL08	5						
Grader	SLS01	8						
5t Excavator	AMG 007							
1.5 Excavator	AMG 009	5						
5t Excavator	AA 25	5						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					
Total Plant and Equipment Hours:		57						

DELAYS-OPPORTUNITY

Porters advised that City of Greater Geraldton have rejected extension of Forrest Street Paving Area to accommodate additional services

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Speaking up
TCD - Daily Safety Focus:	Plant on Plant Interaction
Hazards Reported:	Nil
Incident Free Days	74
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-05 Scheme D implemented

Progress Meeting

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Ongoing underground Services

Rebuilding of verges

Placed material for laneway road widening

Ongoing Subgrade Prep

Photos





TCD DAILY FIELD REPORT

Project Name:	Batavia Station Square	Date:	7/08/2025
Project Location:	Geraldton	Day:	Thursday
Project Number:	TCD-1816	Start:	7:00
Report Number:	73	Finish:	17:00

WEATHER & GROUND CONDITIONS

Temperature: 24 degrees Wind 52km/h N Precip: 0 mm

PERSONNEL

TCD Indirects			TCD Directs			Subcontractors		
Name	Position	Hours	Name	Position	Hours	Name	Position	Hours
WATKINS, Steve	Civil Manager					Khegan Brockman	Labourer	10
GRIFFITHS, Daniel	Project Manager	10				Laurent Levy	Operator	10
O'SHEA, John	Senior Project Engineer	10				Daniel McAuffile	Operator	10
GRIFFITHS, Ashley	Supervisor	10				O'Brian, Jamie	Operator	10
LOW, June	HSET					Simpson, Josh	Operator	10
SKINNER, Jamie	Supervisor	10				O'Reilly, James	Operator	10
						Chester, Matt	Gas Fitter	
						Mounsey, Matt	Gas Fitter	
						Herring, Levin	Gas Fitter	
Total Indirect Personnel onsite:	4					Total Subcontractor on-site:	6	
Total Indirect Personnel hours:	40					Total Subcontractor hours:	60	
Total Direct Personnel onsite:	0							
Total Direct Personnel hours:	0							

PLANT & EQUIPMENT

Plant	ID	Hours	Vehicles	ID	QTY	Site Facilities	ID	Qty
Komatsu WA320	FWL18	7	Hilux	DLV90	1	Office 40ft	9255540	1
Wacker Neuson DPU	DPC15	5	6 Wheel Tipper	AMG04		Sea Container 20ft	951200	1
Positrak	AMG 025	5				Site Sentry Tower		2
Watrcart	WC04	8				Skip Bin		1
8T Excavator	AMG 014	6				Hydrocarbon Bund		1
6 Wheel Tipper	AMG 008					Temp Fence		1
Padfoot/ Smooth Drum Roller	RR 03	10						
Positrak SSL	SSL08	10						
Grader	SLS01	10						
5t Excavator	AMG 007							
1.5 Excavator	AMG 009	5						
5t Excavator	AA 25	10						
0	Repairs Required		N/A					
0	Scheduled Service		N/A					
0	Repairs required but operable		N/A					

Total Plant and Equipment Hours: 76

DELAYS-OPPORTUNITY

HSEQ MESSAGES

TCD - Monthly Safety Focus:	Speaking up
TCD - Daily Safety Focus:	Wind and dust
Hazards Reported:	Nil
Incident Free Days	75
Other Notes	

INCIDENTS & REPORTS

	QTY	Comments
INCIDENT	0	NA
IR	0	NA
NCR	0	NA

COMMUNICATIONS

TGS MB1119-05 Scheme D implemented

PRODUCTION (CONSTRUCTION STATUS & PROGRESS)

Ongoing cutting of Drainage pits
 Denso Tape of water risers (inspected by WC)
 Install headwall in sump
 Ongoing Subgrade Prep

Photos

